



ISD #381

Lake Superior Schools

Minnehaha Elementary School

ICS Weekly Progress Report

Friday – July 12, 2024

Address: 421 7th Street Two Harbors, MN 55616

Minnehaha Elementary School

Completed week July 12, 2024

- Demolition Wrapping up.
- Framing of soffits at Ceilings continues
- Cabinet installs in Kindergarten Suite
- Cutting masonry openings for windows. scopes continue.
- Saw cutting of Masonry walls and new window openings.
- Earthwork at sidewalk/playground area.
- Underground plumbing.
- Rain Leader corrective work in area C.
- Hang and install doors and hardware in area C.
- Masonry entrances at classroom build backs.
- Painting throughout

Upcoming Work

- Ceiling Grid continues.
- Lights begin to be installed in Classrooms.
- Earthwork at sidewalk/playground area.
- Framing walls and Soffits
- Quarry tile work in storage area.
- Underground plumbing pour backs
- Install hollow metal door frames throughout.
- Rain Leader corrective work in area C.



ISD #381
Lake Superior Schools
Minnehaha Elementary School

ICS Weekly Progress Report
Friday – July 12, 2024

Address: 421 7th Street Two Harbors, MN 55616

Progress Photos




Cabinet Install Continues where ready.



ISD #381
Lake Superior Schools
Minnehaha Elementary School

ICS Weekly Progress Report
Friday – July 12, 2024

Address: 421 7th Street Two Harbors, MN 55616

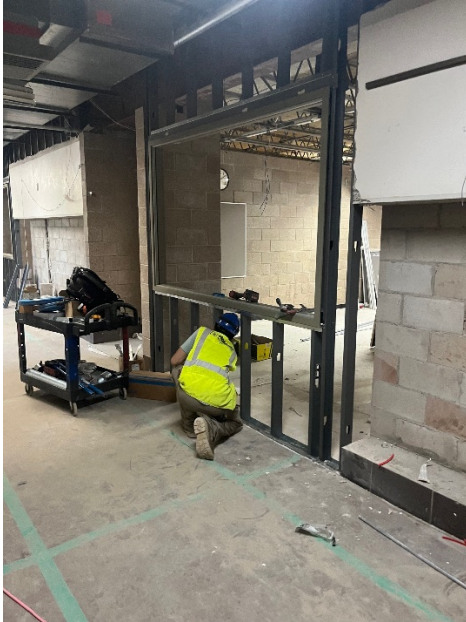

Steel Stud Framing areas.



Earthwork at Sidewalk/Turf Area.



ISD #381
Lake Superior Schools
Minnehaha Elementary School

ICS Weekly Progress Report
Friday – July 12, 2024

Address: 421 7th Street Two Harbors, MN 55616



Painting Throughout
