



ISD #381

Lake Superior Schools

William Kelley Addition and Renovation

ICS Weekly Progress Report

Friday – May 24, 2024

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

William Kelley Addition and Renovation



Completed week ending May 24, 2024

-  Continued exterior wall framing for Area B Music Suite
-  Roofing Area B Music Suite
-  Poured floor for Area B Music Suite
-  Painting in boys' locker room.
-  Continue wall framing in girls' locker room
-  Mechanical and electrical rough ins for girls' locker room
-  Plumbing inspection in girls' locker room
-  Demolition in kitchen
-  Demolition in old Admin area
-  Demolition at competition gym
-  Demolition in old art room/new FACS



Upcoming planned work

-  Continue exterior wall framing for Area B Music Suite
-  Continue roofing Area B Music Suite
-  Pour concrete stairs and ramp for Area B Music Suite
-  Interior wall framing in Area B Music Suite
-  Roof drain piping in Area B Music Suite
-  Continue painting in boys' locker room.
-  Drywall wall framing in girls' locker room
-  Underground plumbing in kitchen
-  Wall framing in old Admin area
-  Continue demolition in competition gym
-  Finish demolition in art room/new FACS



ISD #381

Lake Superior Schools


William Kelley Addition and Renovation

ICS Weekly Progress Report

Friday – May 24, 2024

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

Progress Photos

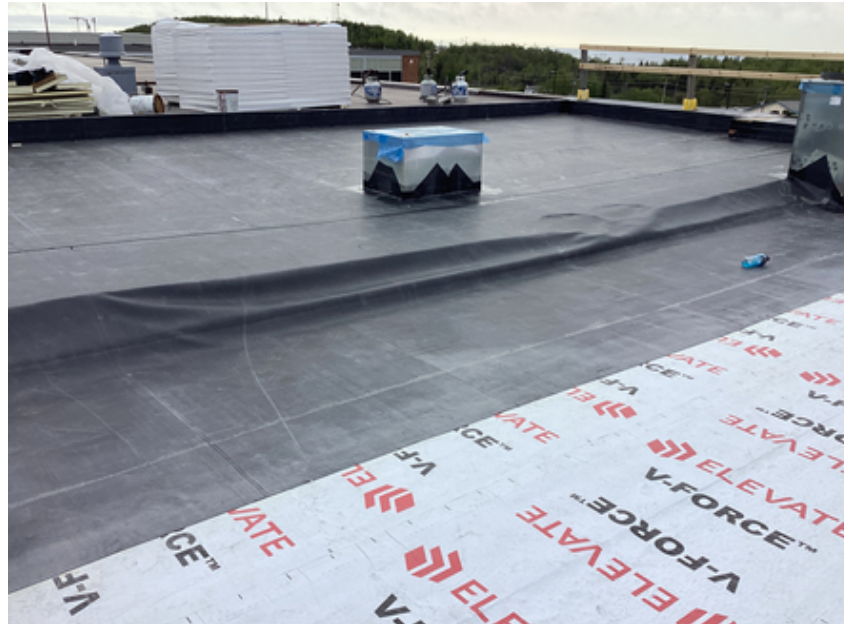

Roofing delivery and staging for Area B Music Suite



Floor poured at Area B Music Suite



ISD #381

Lake Superior Schools
William Kelley Addition and Renovation

ICS Weekly Progress Report
Friday – May 24, 2024

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614



Upper level exterior wall at Area B Music Suite



Kitchen demolition and floor removal



ISD #381

Lake Superior Schools

William Kelley Addition and Renovation

ICS Weekly Progress Report

Friday – May 24, 2024

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614



Old FACS main level Area C demolition



Competition gym demolition
